STARTUP EXECUTION PLAN | VERSION 1.0 | NOVEMBER 2026

OmniSight AI

Your expert in your ear, in your language.

AI smart glasses that guide deskless workers hands-free, step by step

Contents

Step 1	Executive Summary	2
Step 2	Problem and Market	3
Step 3	Solution and Product Scope	4
Step 4	Competitor and Positioning Analysis	6
Step 5	Business Model and Pricing	7
Step 6	Go-to-Market Plan	8
Step 7	Operations and Team	9
Step 8	Legal, Regulatory and Risk	10
Step 9	Execution Timeline	11
Step 10	Financial Plan	12
Step 11	Metrics and KPIs	14
Step 12	Next Actions	15

At a glance

Funding ask: PKR 21M pre-seed (base-case peak need PKR 16.2M plus 25% buffer)

Monthly break-even: Mar-28 (month 17) | Target: 250 paying workers by Oct 2027

Every figure is a planning assumption (A) unless a source is named, to be validated in the first 30 days.

Living document: review monthly. Each step also exists as a separate PDF.

STEP 1 OF 12

Executive Summary

Problem, solution, target customer, goals and needs on one page

One-line pitch. OmniSight AI is a pair of smart glasses with a camera and microphone, connected to a back-end AI system that sees what the worker sees and guides them hands-free, step by step, by voice.

Problem. Deskless workers (mechanics, electricians, factory operators and engineers) must stop mid-job to check manuals on a phone or laptop, or call a senior. With dirty hands this wastes time, slows training, causes mistakes and can damage devices.

Solution. The worker wears smart glasses. The camera streams what they see and the microphone takes their questions. A back-end AI system identifies the machine and fault, checks safety, and speaks instructions into the worker's ear (for example, "Remove the right-hand bolt"). If the AI is unsure, it escalates to a human expert.

Target customer. Companies with maintenance and service teams: auto service centres, factories, electrical contractors and similar. First city: Karachi, then Lahore and Islamabad. The company pays a monthly subscription per worker.

Why now, why us. Enterprise AR tools usually rely on a remote human expert and expensive headsets. Our back-end AI works without an expert on the call and runs on lower-cost consumer-grade smart glasses, with Urdu and Roman Urdu voice. Access to glasses software platforms is a risk we manage by being hardware-agnostic.

Business at a glance

Item	Plan
Product	Smart-glasses app plus cloud back-end AI for guided field work
Revenue model	Subscription: PKR 5,000 per worker per month (A); glasses supplied at cost
Launch city	Karachi (pilot Feb-Mar 2027, paid launch Apr 2027)
90-day goal	By Sun 7 Feb 2027: prototype working on glasses, 3 signed pilot letters, pilot starting with 20 workers, 30 interviews done
12-month goal	250 paying workers (about 17 companies) and PKR 1.25M monthly revenue by Oct 2027 (A)
Break-even (monthly)	Mar-28 (month 17), base case
Funding needed	PKR 21M pre-seed (base-case need PKR 16.2M plus 25% buffer, rounded up)

What we need

- **Funding:** PKR 21M pre-seed, released in milestone tranches (Step 10).
- **Partners:** 3 to 5 pilot companies; 2 to 3 smart-glasses suppliers; one or more equipment distributors.
- **People:** a core team of 6 (CEO, CTO, product lead, sales lead, AI engineer, glasses-app developer) plus part-time industry experts and an outsourced accountant and lawyer.

All figures in this plan are planning assumptions marked (A) unless a source is named. No third-party market statistics are used; each assumption is tested in the validation work in Step 9. PKR = Pakistani rupee.

STEP 2 OF 12


Problem and Market

Who has the problem, how painful it is, and how big the opportunity is

Who has the problem. People who work away from a desk: deskless workers (mechanics, electricians, factory operators and engineers). In the field, a worker meets machines, faults and procedures they may not know. Information is in manuals, on phones, or in a senior colleague's head.


How painful it is. Hands are busy or dirty, so checking a screen means stopping work. Searching and waiting slow the job; guessing causes rework and risks injury or damaged equipment. New workers take long to train. These are founders' hypotheses, tested in 30 interviews and a 100-response survey by day 30.

Hypothesis: where a worker's time goes



Source: founders' hypothesis (A). The 50/25/15/10 split will be replaced by interview findings.

Market size (bottom-up)

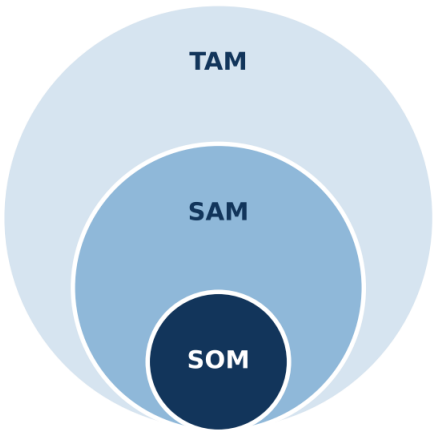

TAM: PKR 60B / year

1,000,000 deskless maintenance, repair and plant workers in Pakistan x PKR 5,000 x 12 months (A1)

SAM: PKR 3.0B / year

50,000 workers (5% of TAM) employed by mid-size and large organisations in Karachi, Lahore, Islamabad (A2)

SOM: PKR 15M / year

250 paying workers (about 17 companies) by Oct 2027 = 0.5% of SAM (A3)

A = planning assumption, to be validated by day 30 (Step 9)

Ref	Assumption	Value	How we will validate it
A1	Deskless maintenance, repair and plant workers in Pakistan	1,000,000	Labour force data, industry bodies, company interviews (to be checked)
A2	Share employed by mid-size and large organisations in the 3 target cities	5% (50,000)	Company counts and headcount from interviews
A3	Paying workers by Oct 2027	250 (about 17 companies)	Pilot conversion and sales tracking
A4	Price per worker per month	PKR 5,000	Willingness-to-pay questions in interviews

Reading the numbers. TAM and SAM use the full list price for every worker and are an upper bound, not a forecast. SOM drives the plan and the financial model in Step 10.

All figures in this plan are planning assumptions marked (A) unless a source is named. No third-party market statistics are used; each assumption is tested in the validation work in Step 9. PKR = Pakistani rupee.

STEP 3 OF 12


Solution and Product Scope

Core features, MVP boundary, system design, user journey and feature roadmap

Core features (MVP)


Feature	What it does	Why it matters
Smart-glasses capture	Camera and microphone stream what the worker sees and says	Hands-free, no screen
Voice Q and A	Worker asks in Roman Urdu, Urdu or English; answers by voice	Natural, fast
Machine and fault recognition	Back-end vision AI identifies the machine, label, part or error	Removes manual searching
Guided procedures	Step-by-step instructions from the company's own approved manuals	Correct, consistent work
Safety checks	Mandatory checks before risky steps; refuses to guess on high-risk tasks	Protects people and equipment
Escalation	Shares live view and job notes with a human expert when unsure	Safe fallback
Job log	Records job, machine, time and result	Proof of work and training data

System design

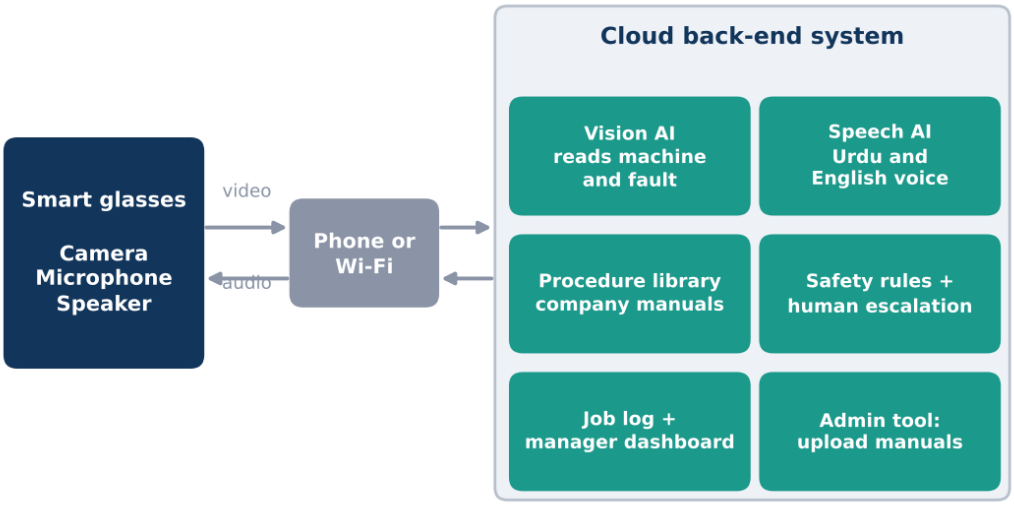


The glasses are the eyes, ears and speaker. All heavy AI work runs in the back-end, so the glasses stay light and low-cost.

User journey flow

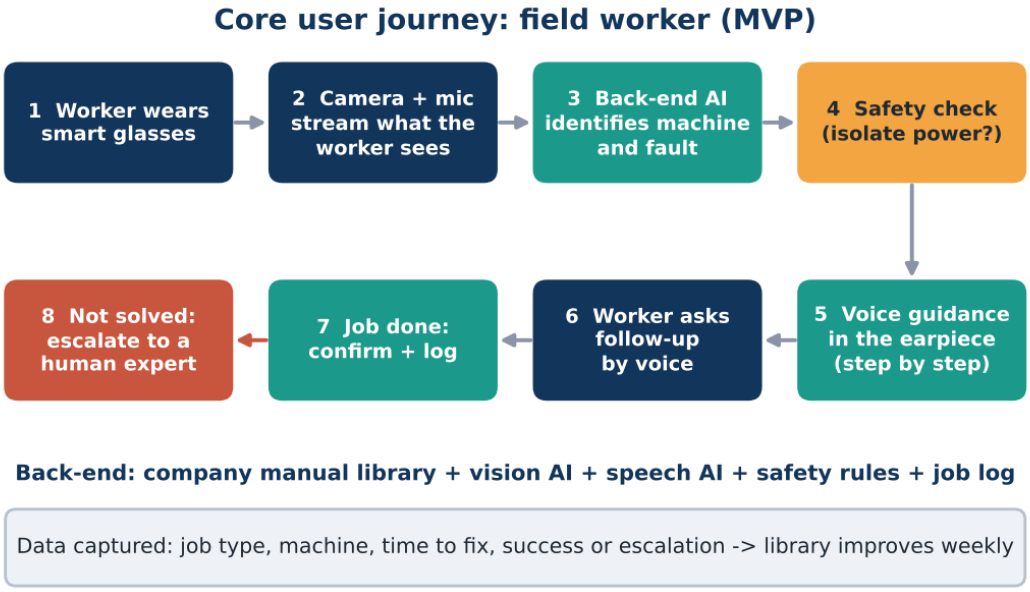

Feature roadmap

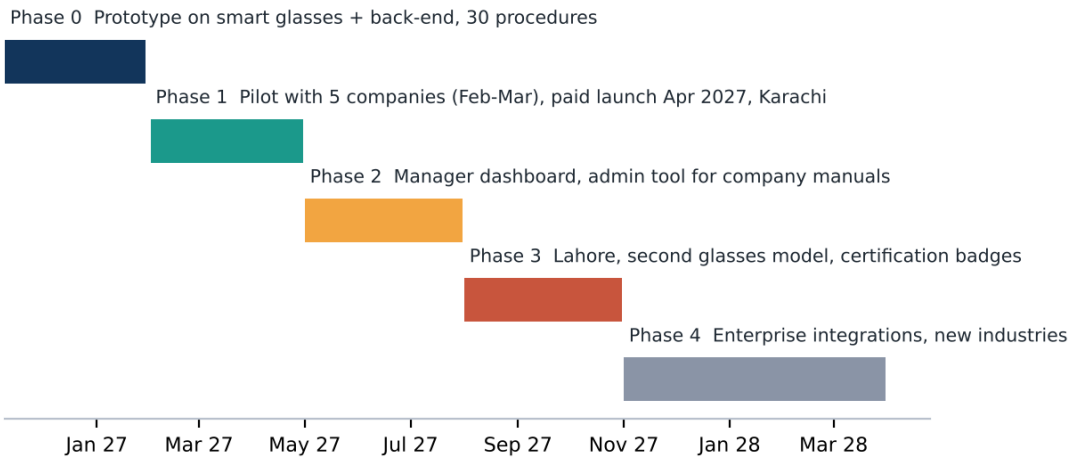

MVP boundary

In the MVP	Not built yet (and why)
One supported smart-glasses model plus an Android companion app; cloud back-end; Roman Urdu, Urdu, English; 30 procedures, growing to 100; Karachi; 2 or 3 industries chosen after interviews	Own-brand hardware (cost, time); display or AR-overlay glasses; iOS; offline mode; ERP integrations; other languages; manager dashboard and manual-upload admin tool (Phase 2)

Design rule: the AI answers only from the company's approved procedure library. If a procedure is missing or confidence is low, it says so and escalates, instead of improvising.

STEP 4 OF 12

Competitor and Positioning Analysis


Direct and indirect competitors, 2x2 matrix and our unfair advantage

Direct competitors are AR and connected-worker platforms and industrial headsets. **Indirect competitors** are the ways workers solve problems today. Descriptions are the founders' initial assessment from public information and must be re-verified before any investor pitch.

Comparison table

Competitor	Type	Likely strength	Gap versus OmniSight (to verify)
Microsoft Dynamics 365 Guides / Remote Assist	Direct (enterprise)	Mature product, enterprise integration	Built for large organisations; often relies on a remote human expert; English-first
TeamViewer Frontline	Direct (enterprise)	Workflow and remote support tools	Enterprise pricing and onboarding; expert-led
PTC Vuforia, Augmentir, Taqtile	Direct (enterprise)	AR work instructions, connected-worker analytics	Aimed at large factories and utilities
RealWear, Vuzix	Direct (hardware)	Rugged hands-free headsets	Costly hardware; we use lower-cost consumer-grade glasses
Consumer AI glasses (for example Ray-Ban Meta)	Partner and future competitor	Low cost, camera, mic, assistant	Not built for industrial work or company manuals; developer access must be verified
Remote video-call tools	Indirect	Cheap, familiar	Needs a human expert online at the same time
General AI chatbots	Indirect	Cheap, flexible	No glasses workflow, no company manuals, no safety rules
YouTube, WhatsApp, senior (ustad), paper manuals	Indirect	Free, trusted	Not step-by-step, not model-specific, not always available

2x2 positioning matrix

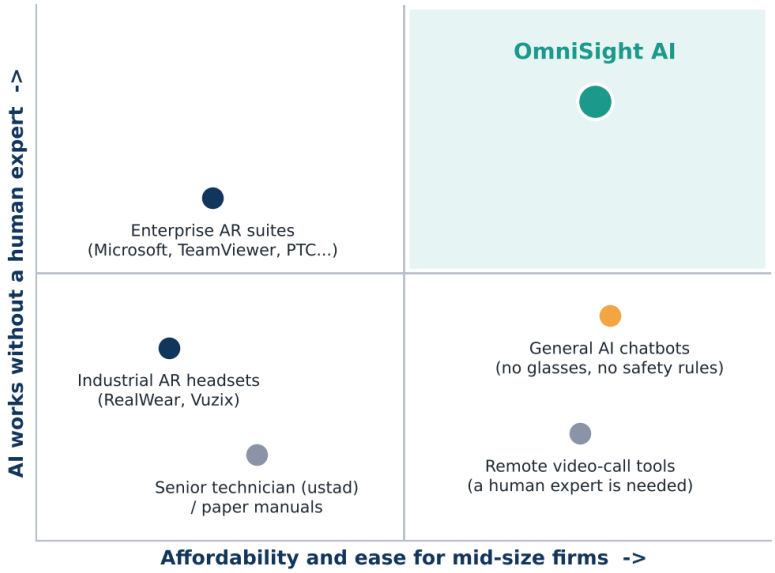

Placement is qualitative (founders' judgement). Horizontal: affordability and ease for mid-size firms. Vertical: how well the AI guides without a human expert.

Our unfair advantage (to be built, not yet proven)

- **No human behind the screen:** an autonomous multimodal AI guides the worker; experts are only a fallback.
- **Lower cost:** software for consumer-grade smart glasses instead of costly industrial headsets.

- **Local-language voice:** Roman Urdu and Urdu guidance tuned to workshop and factory vocabulary.
- **Company manuals:** each customer's own approved procedures become the AI's knowledge.
- **Safety-first design:** approved-procedure-only answers and mandatory safety checks.


Risk: large platforms or glasses makers could add similar features. Our defence is customer-specific data, local language, partnerships and being hardware-agnostic.

STEP 5 OF 12

Business Model and Pricing

Revenue streams, pricing logic and unit economics

How we make money

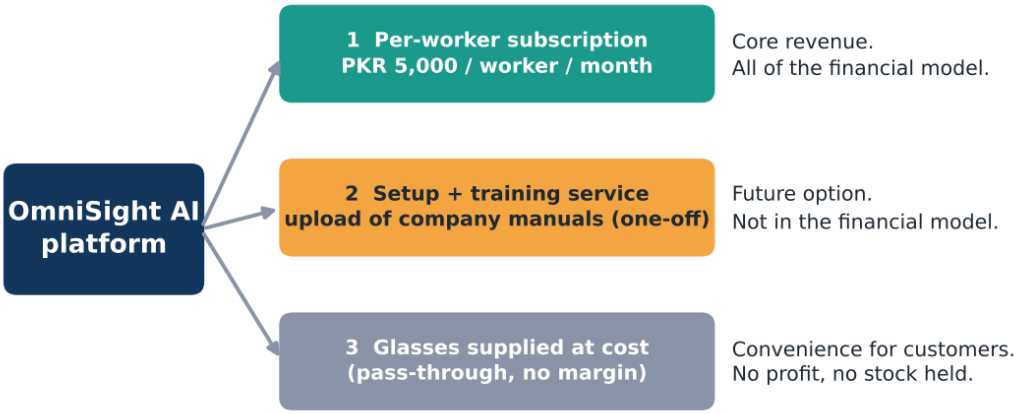

Plan	Price (A)	Who it is for
Standard	PKR 5,000 per worker per month, minimum 5 workers	Maintenance and service teams
Annual prepay	10 months' price for 12 (about 17% off)	Companies that prefer a yearly contract
Enterprise	Custom price for 50+ workers, manual set-up included	Large factories and fleets

Pricing logic

- PKR 5,000 a month is about PKR 192 per working day (26 days). It pays for itself if it saves the worker's company roughly that much paid time or rework (tested in the pilot).
- Priced per worker because value and AI usage scale with each worker.
- Glasses are bought by the customer or supplied at cost through a supplier, so we hold no stock and take no hardware margin. This keeps our cash need lower.

Unit economics (per worker)

Metric	Value	How it is derived
Revenue per worker per month	PKR 5,000 (A)	List price
Variable cost per worker per month	PKR 1,200 (A)	Video and AI processing, cloud, support
Gross margin per worker per month	PKR 3,800 (76%)	Revenue minus variable cost
Customer acquisition cost (CAC)	PKR 300,000 per company = PKR 20,000 per worker (A)	Sales effort and pilot cost; 15 workers per company (A)
Monthly churn	4% (A)	Average lifetime = 1 / churn = 25 months
Lifetime gross profit (LTV)	PKR 95,000	Gross margin x average lifetime
LTV to CAC ratio	4.8x	Healthy if above 3x; to be proven in the pilot
CAC payback	Month 6	Cumulative gross profit, allowing for churn



Churn, CAC and variable cost are the most uncertain inputs. Step 10 shows what happens if they are worse than planned.

STEP 6 OF 12

Go-to-Market Plan

Channels, early customers, partnerships and messaging


Positioning message

"Your expert in your ear, in your language." Hands-free, step-by-step help on every job, with safety checks built in.

Channels and early customer sources

Channel	How it works	Owner	Phase
Direct sales to maintenance and operations managers	Demo with real equipment; offer an 8-week pilot	Head of Sales	Pilot onward
Equipment distributors and service networks	Co-selling to the companies and technicians they already serve	CEO + Head of Sales	Pilot onward
Smart-glasses suppliers	Bundle: glasses at cost plus our software	Head of Sales	Pilot onward
Industry associations, trade events	Demos and case studies	CEO	Phase 1
LinkedIn and WhatsApp outreach	Short demo videos of real jobs	Head of Sales	Pilot onward
Referral	One free month for the referring company	Product	Phase 1

Funnel (assumed conversion rates)



12 paying companies x 15 workers = about 180 paying workers. All rates are assumptions (A) to be measured.

The pilot success test: at least 80% of guided jobs rated solved by the worker, and at least 50% of pilot companies sign a paid plan. Rates are assumptions to be measured.


Partnerships to pursue first

- Three to five pilot companies in Karachi (target: signed letters of intent by day 60).
- Two or three smart-glasses suppliers: price quotes, import support and developer access.
- One or two equipment distributors with service networks.

STEP 7 OF 12

Operations and Team

Organization chart, roles, tools and outsourced work

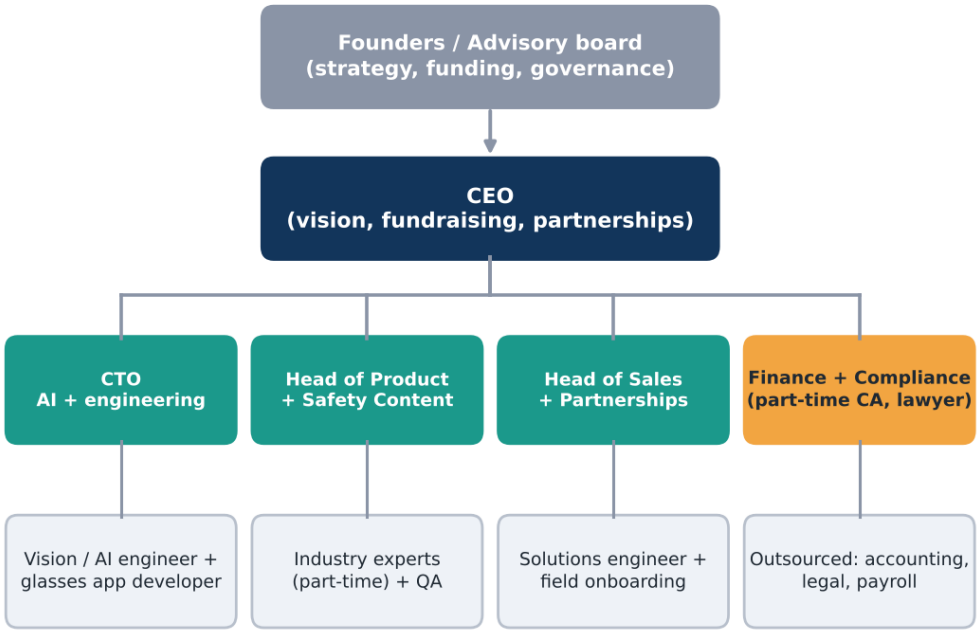

Phase 1 (Nov 2026 to Apr 2027): 6 core people. Phase 2 (from May 2027): add a solutions engineer, sales support and a second engineer. Payroll assumptions are in Step 10.

Roles and responsibilities

Role	Responsibilities	Type
CEO	Vision, fundraising, investor and partner relations, hiring, monthly review of this plan	Core, full-time
CTO	AI architecture, vision and voice pipeline, security, releases, vendor choice	Core, full-time
Head of Product and Safety Content	Procedure library, safety rules, expert reviewers, user research, roadmap	Core, full-time
Head of Sales and Partnerships	Pilot companies, distributors, glasses suppliers, pricing, sales targets	Core, full-time
AI engineer (vision and speech)	Build and evaluate the recognition and guidance models	Core, full-time
Glasses app developer	Glasses and companion app, streaming, device testing	Core, full-time
Industry experts	Write and review procedures; test safety	Part-time, paid per procedure
Finance and compliance	Bookkeeping, tax, company compliance, contracts, privacy policy	Outsourced (chartered accountant, lawyer)

Tools

- **Build:** GitHub, a major cloud provider with GPU capacity, a model-agnostic AI layer (no lock-in to one vendor), device test lab with 2 or 3 glasses models.
- **Work:** shared drive and documents, task board, WhatsApp Business for customer support.
- **Finance:** accounting software and a monthly cash dashboard.

Outsourced work: legal, accounting and tax, hardware import and logistics, video production. Decision rights: CEO decides on funding and partnerships; CTO on technology; Product lead on safety rules (a safety decision can only be overruled by a unanimous founder vote).

STEP 8 OF 12

Legal, Regulatory and Risk

Licences, compliance, data protection and key risks

Licences and compliance checklist

These items must be confirmed with a qualified lawyer, tax adviser and customs broker before launch, because requirements and rates change.

Item	What to do	Owner
Company	Incorporate a private limited company with SECP; shareholders' agreement and vesting	CEO + lawyer
Tax	Obtain NTN from FBR; check sales tax on services registration (provincial authority, for example Sindh Revenue Board for Karachi) and withholding rules	Finance
Banking	Open a company account; B2B invoicing by bank transfer	Finance
Hardware import	Customs duties and approval of wireless devices (check requirements with a customs broker); or buy locally from a supplier	Sales + Finance
Software exporter benefits	Check whether PSEB registration is useful	Finance
Terms and Privacy	Terms of use, safety disclaimer, workplace recording policy, privacy policy	Lawyer
Data protection	Review applicable Pakistani law on personal data, including the status of draft data protection legislation	Lawyer
Contracts	Customer, supplier, expert and employee agreements; IP assignment	Lawyer

Risk table (risk, impact, mitigation)


Risk	Impact	Mitigation
Unsafe guidance causes injury or equipment damage	High	Approved-procedure-only answers; mandatory safety checks; refuse or escalate for high-voltage and other high-risk tasks; terms of use with safety disclaimer; review insurance options with a lawyer
AI gives a wrong or invented answer	High	Retrieval from the company's approved library only; confidence threshold; report button; weekly expert review of flagged answers
Privacy: cameras record colleagues, customers and premises	High	Consent and workplace policy; visible recording indicator; no face storage; blurring where possible; short retention (30 days for raw video); privacy policy
Hardware: cost, battery, import and device approval	High	Hardware-agnostic software; supplier quotes; check customs duties and wireless device approval before import; pilot with 20 pairs only
Dependence on a glasses maker or AI vendor	Medium	Support more than one glasses model; model-agnostic back-end; treat developer access as a risk, not a plan; verify before building
Poor mobile data or Wi-Fi on site	Medium	Low-bandwidth video, audio-first mode, on-site Wi-Fi setup; offline mode planned
Worker or union acceptance (fear of being monitored)	Medium	Position as a helper, not a monitor; no individual scoring in the MVP; involve workers in the pilot
Company manuals are confidential or copyrighted	Medium	Customer owns its data; written permission for manuals; private data separation per customer
Longer B2B sales cycle than planned	Medium	Pilot-led selling; 3-month delay tested in Step 10
Running out of cash	High	Milestone-based funding; 25% buffer; monthly cash review; cost cuts ready

STEP 9 OF 12

Execution Timeline

Milestones, owners and deadlines: 30, 60, 90 days and a 12-month Gantt chart

Start date: Mon 9 Nov 2026 (Day 0). Day 30, 60 and 90 are counted from this date.

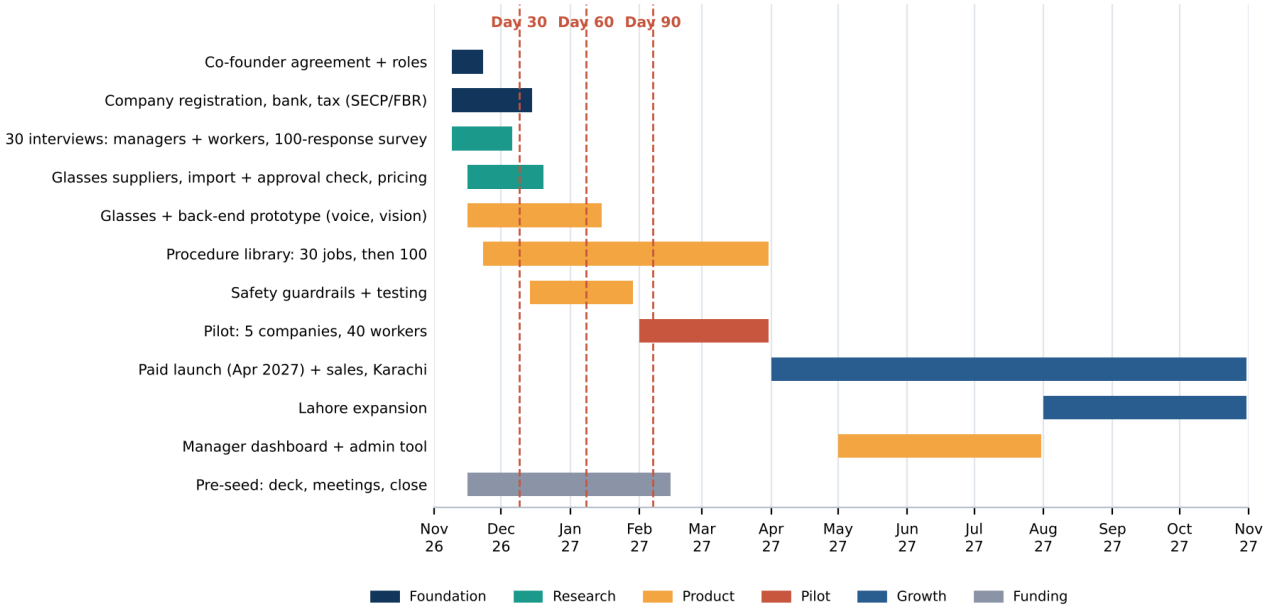

Gantt chart: 12-month plan, November 2026 to October 2027. Red dashed lines mark day 30, 60 and 90.

30 / 60 / 90 day milestones

By	Milestone	Owner	Done when
Day 30 Wed 9 Dec 2026	30 interviews done; target industries, price and pilot companies shortlisted; company registration filed; first prototype (phone camera plus back-end) demo	Head of Product; Head of Sales; CEO; CTO	30 interviews and 100 survey responses logged; filing receipt; demo recorded
Day 60 Fri 8 Jan 2027	Prototype running on smart glasses with voice and vision; 30 procedures; 3 pilot letters signed; glasses supplier chosen; first investor meetings	CTO; Head of Product; Head of Sales; CEO	Live demo on glasses; 3 signed letters; supplier quote
Day 90 Sun 7 Feb 2027	Pilot starts with 20 workers; safety guardrails tested; success test defined	CEO; all heads	Pilot kit in use at 3 companies
Month 6 30 Apr 2027	Pilot finished (40 workers); paid launch; 30 paying workers; 100 procedures	Head of Sales; Head of Product	At least 80% jobs solved; at least 50% of pilot companies pay
Month 12 31 Oct 2027	250 paying workers (about 17 companies); PKR 1.25M monthly revenue; Lahore started	CEO	Revenue and user dashboard

STEP 10 OF 12

Financial Plan

Budget, 12 to 24 month forecast, break-even, runway and funding needs


Key assumptions

Item	Assumption (A)
Price	PKR 5,000 per paying worker per month; no discounts modelled
Pilot	Feb-Mar 2027: 20 then 40 free pilot workers; 20 glasses kits bought for PKR 1.2M (about PKR 60,000 each, to be confirmed by supplier quotes)
Paying workers	Apr 2027: 30; Jul 2027: 100; Oct 2027: 250; Apr 2028: 700; Oct 2028: 1,500 (straight-line between points)
Variable cost	PKR 1,200 per active worker per month
Payroll	PKR 700,000 per month (Nov 2026 to Apr 2027); PKR 1,000,000 (May to Oct 2027); PKR 1,500,000 (from Nov 2027)
Other fixed costs	PKR 200,000 per month in year 1; PKR 300,000 from year 2 (cloud base, GPU, tools, co-working, legal, accounting)
Marketing and sales	PKR 100,000 per month to Feb 2027; PKR 300,000 for the rest of year 1; PKR 450,000 from year 2
One-off setup	PKR 400,000 in month 1 (registration, legal, brand)
Funding	Modelled as available from month 1 (simplification); released in tranches in practice

Budget and forecast summary


	First 12 months (Nov 2026 to Oct 2027)	24 months (to Oct 2028)
Revenue	PKR 4.3M	PKR 54.7M
Total cost	PKR 18.1M	PKR 57.2M
Net result	PKR -13.8M	PKR -2.5M
Lowest cumulative cash need	PKR 16.2M (reached Feb-28)	

Revenue and cost

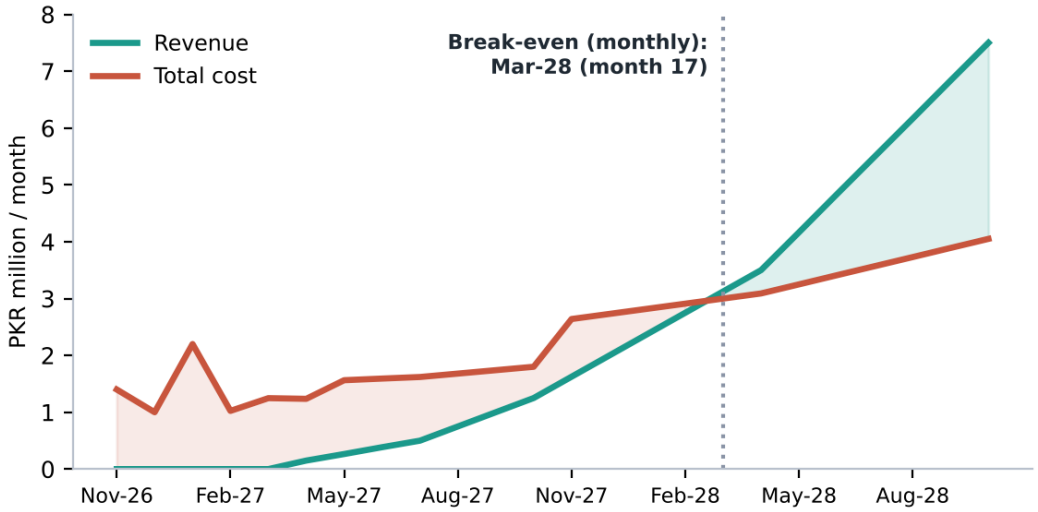

Monthly break-even: Mar-28 (month 17). Cumulative cash does not turn positive within the 24 months of the model.

Runway and funding

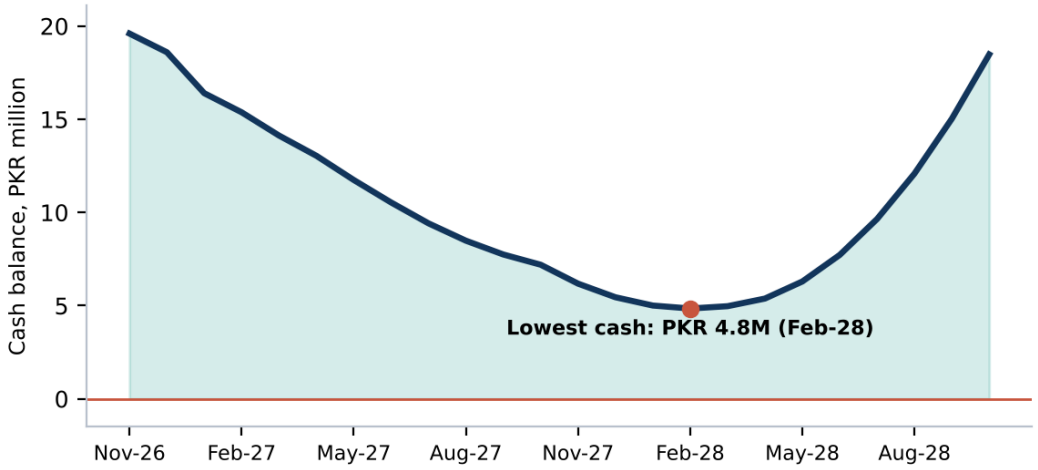

Funding ask: PKR 21M. Base-case peak funding need is PKR 16.2M. We add a 25% buffer and round up to PKR 21M. Cash does not fall below PKR 4.8M in the base case. Release in tranches tied to the pilot result (Apr 2027) and the month-12 targets.

Where the money goes: base-case costs, months 1 to 17 (partly covered by revenue)

Use	PKR	Share of cost
People (payroll)	PKR 17.7M	55%
Marketing and sales	PKR 5.0M	16%
Variable cost (AI, cloud, support)	PKR 4.0M	12%
Pilot glasses kits	PKR 1.2M	4%
Other fixed and setup	PKR 4.3M	13%
Total cost until monthly break-even	PKR 32.2M	100%

Sensitivity: what if we are wrong?

Scenario	Monthly break-even	Peak funding need (before buffer)
Base case	Mar-28 (month 17)	PKR 16.2M
Price 20% lower (PKR 4,000)	May-28 (month 19)	PKR 19.6M
Growth 30% lower	Jun-28 (month 20)	PKR 20.1M
Variable cost 50% higher (PKR 1,800)	May-28 (month 19)	PKR 18.0M
Paid launch delayed by 3 months	Jun-28 (month 20)	PKR 22.9M

The PKR 21M ask covers the base case with buffer. The worst case above needs about PKR 22.9M before buffer, which is above the ask. The plan therefore includes cost-cut options (hiring freeze, lower marketing) or a bridge round.

STEP 11 OF 12

Metrics and KPIs

Numbers that show progress, with targets and owners

A short list of numbers that show whether the business is working. Review weekly in the pilot and monthly afterwards.

KPI	Definition	Target	When	Owner
Activation rate	Pilot workers completing 5 guided jobs in 14 days	60%	Pilot onward	Product
Pilot to paid	Pilot companies that sign a paid plan	50%	From Apr 2027	Sales
Task success rate	Guided jobs the worker marks as solved	At least 85%	Pilot onward	Product
Escalation rate	Jobs sent to a human expert	Below 15%	Pilot onward	Product
Unsafe answer incidents	Reported or found safety failures	0 serious	Always	Product + CTO
Response time	Voice question to spoken answer	Under 3 seconds	Prototype	CTO
Paying workers	Active paid subscriptions	30 (Apr 2027); 250 (Oct 2027)	Monthly	Sales
Monthly recurring revenue	Paying workers x PKR 5,000	PKR 150,000 (Apr 2027); PKR 1.2M (Oct 2027)	Monthly	CEO
Monthly churn	Paying workers who leave in the month	4% or lower	Monthly	Sales
CAC	Sales and pilot cost per new paying company	PKR 300,000 or lower	Monthly	Sales + Finance
LTV to CAC	LTV divided by CAC	3x or higher	Quarterly	Finance
Net promoter score	Would you recommend us? (0 to 10)	40 or higher	Quarterly	Product
Cash runway	Months of cash at current spending	At least 9 months	Monthly	CEO + Finance

Scorecard format (fill monthly)

KPI	Target	Actual	Status (green / amber / red)	Action
Activation rate				
Task success rate				
Paying workers				
Monthly recurring revenue				
Monthly churn				
CAC				
Cash runway				

Rule: green means at target; amber within 20% of target; red worse than that. Any red on safety or cash is discussed at the next founder meeting.

STEP 12 OF 12

Next Actions

The next ten tasks, each with an owner and a date

Eleven concrete tasks for the first six weeks. Dates are deadlines. Tick the box when done.

Done	Task	Owner	Deadline
☐	Sign the co-founder agreement (roles, equity, vesting)	CEO	Fri 13 Nov 2026
☐	Finalise interview script and survey; shortlist target industries	Head of Product	Tue 17 Nov 2026
☐	Demo prototype v0: phone camera plus back-end AI guiding one job	CTO	Mon 30 Nov 2026
☐	Draft safety rules and the first 20 approved procedures	Head of Product	Fri 4 Dec 2026
☐	Complete 30 interviews and 100 survey responses	Head of Sales	Sun 6 Dec 2026
☐	First monthly review of this document	CEO	Mon 7 Dec 2026
☐	Get quotes from 3 glasses suppliers; check import and device approval	Head of Sales + Finance	Fri 11 Dec 2026
☐	Meet a lawyer and tax adviser: SECP, FBR, provincial tax, privacy policy	Finance + CEO	Fri 11 Dec 2026
☐	Register the company and open a bank account	CEO + Finance	Tue 15 Dec 2026
☐	Sign 3 pilot letters of intent	Head of Sales	Fri 18 Dec 2026
☐	Finish the investor deck and financial model; start investor meetings	CEO	Sun 20 Dec 2026

After these tasks

- Review the Day-30 results on Wed 9 Dec 2026: confirm industries, price and pilot companies, or change course.
- Update the assumptions (A) in Steps 2, 5 and 10 with real interview and quote data.
- Re-run the financial model and update the funding ask before investor meetings.

Rules for this plan

- Keep the internal plan to 10 to 15 pages and make a shorter version for investors.
- Use visuals only where they speed up understanding.
- Write every number with its source or assumption.
- Treat this as a living document: review it monthly.
